


Job 141 Daily Logs

 Tue, Feb 6

MM Mat McGuire


- Tile Commencement
- Materials delivered to site
- Layout completed with Thanh and Andrei (installer)
- Floor leveller to be installed by Aristocrat
- 2nd coat mud installed in closet


-Closet to be painted by February 13th*

 **Mostly Clear**  19°-35° F  0"  0"  2mph

 **Trades Onsite**

Tile

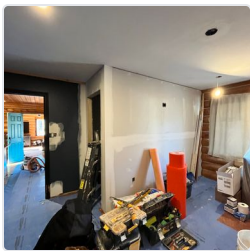



 Fri, Jan 26

MM Mat McGuire

- 2nd coat & tile prep Wednesday (January 31st)
- Drywall completed
- 1st coat mud on
- Site cleaned for 1 week

*Bedroom plugs changed to black (7 receptacles, 2 receptacle + usb, switches)

 **Wintry Mix**  32°-37° F  0.32"  1.15"  6mph

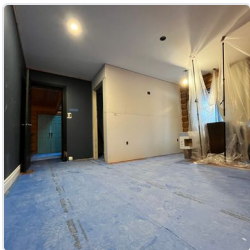


📅 Mon, Jan 22

MM Mat McGuire

- Plumbing rough in inspected for proper locations/leaks
- Bathroom subfloor repaired with new plywood/structural backing where necessary
- underside of floor (top of drop ceiling below) vacuumed and any debris removed
- Floor re-screwed to joists throughout bathroom
- Existing fasteners removed or popped back down into plywood
- Inspected for squeaks in bathroom floor, repaired where necessary
- Site cleaned/protected, ready for next trade

- Electrical walk through performed, fixture locations confirmed
- Electrical rough in commenced

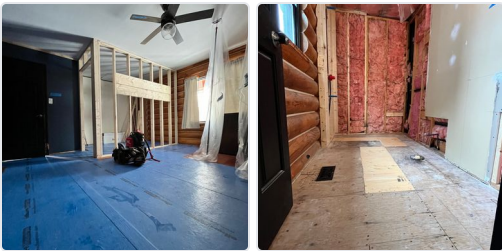

☁ **Blowing Snow** 🌡 20°-30° F 🌊 0.02" ❄ 0.12" 🌀 7mph

☰ **Trades Onsite**

Electrical, Carpentry

T **Internal Notes**

-Verhoef arrived for 3pm, to be completed by end of day January 22nd
