EDEN BUILD
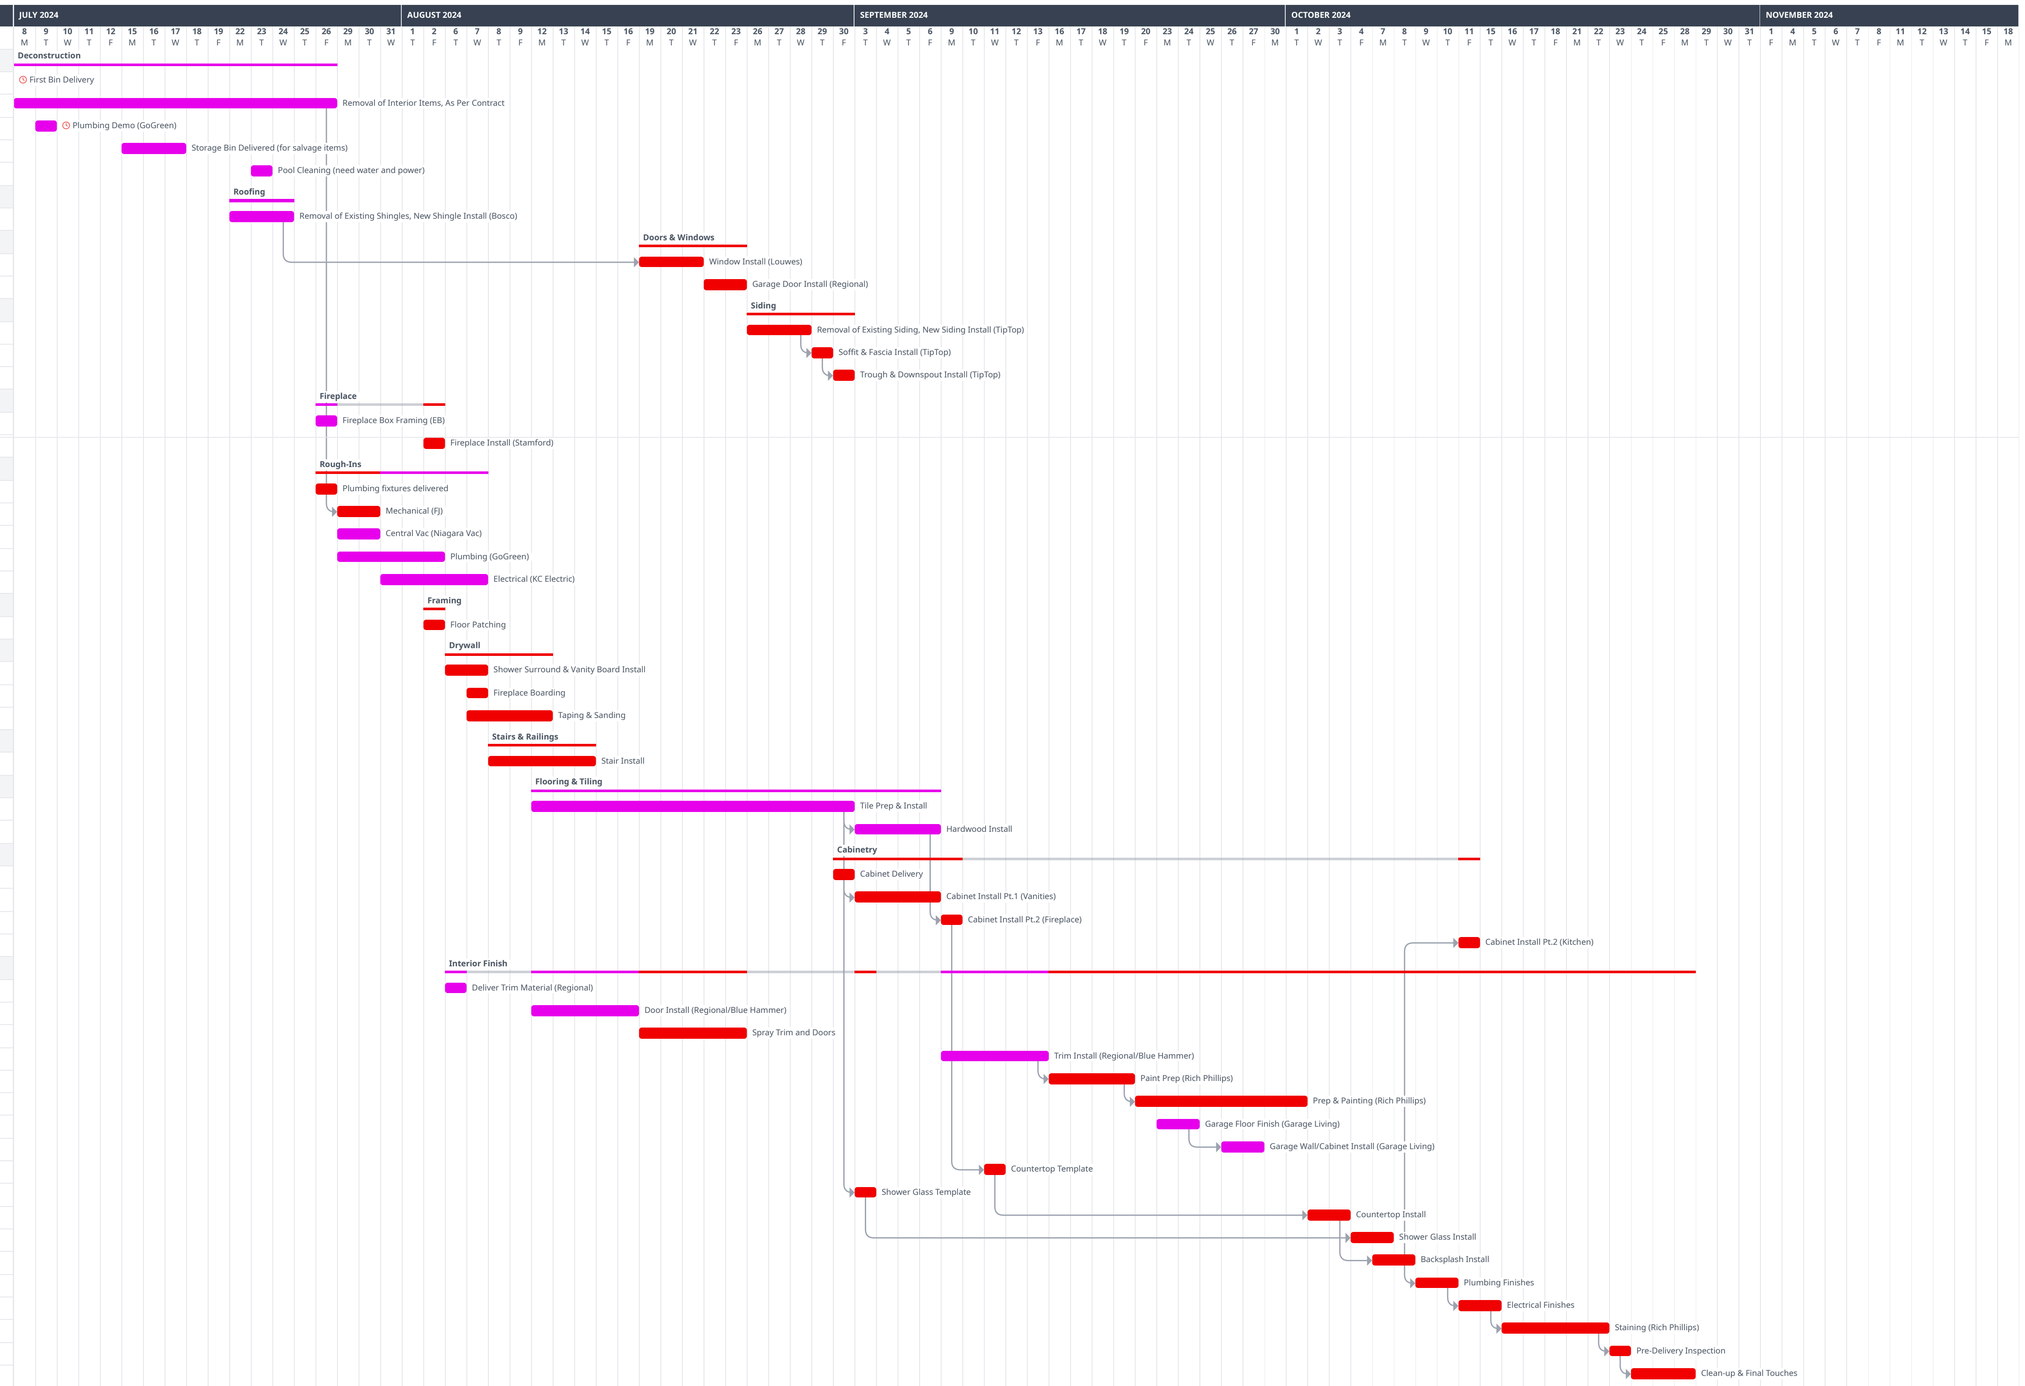
NAME	%	✓	📅	🕒	👥
Overall		☐	Mon, Jul 8	78	
Deconstruction		☐	Mon, Jul 8	15	
First Bin Delivery		☐	Mon, Jul 8	1	
Removal of Interior Items, As Per Contract		☐	Mon, Jul 8	15	
Plumbing Demo (GoGreen)		☐	Tue, Jul 9	1	
Storage Bin Delivered (for salvage items)		☐	Yesterday	3	
Pool Cleaning (need water and power)		☐	Tue, Jul 23	1	
Roofing		☐	Mon, Jul 22	3	
Removal of Existing Shingles, New Shingle Install (Bo:		☐	Mon, Jul 22	3	
Doors & Windows		☐	Mon, Aug 19	5	
Window Install (Louwes)		☐	Mon, Aug 19	3	
Garage Door Install (Regional)		☐	Thu, Aug 22	2	
Siding		☐	Mon, Aug 26	5	
Removal of Existing Siding, New Siding Install (TipTop		☐	Mon, Aug 26	3	
Soffit & Fascia Install (TipTop)		☐	Thu, Aug 29	1	
Trough & Downspout Install (TipTop)		☐	Fri, Aug 30	1	
Fireplace		☐	Fri, Jul 26	6	
Fireplace Box Framing (EB)		☐	Fri, Jul 26	1	
Fireplace Install (Stamford)		☐	Fri, Aug 2	1	
Rough-Ins		☐	Fri, Jul 26	8	
Plumbing fixtures delivered		☐	Fri, Jul 26	1	
Mechanical (FJ)		☐	Mon, Jul 29	2	
Central Vac (Niagara Vac)		☐	Mon, Jul 29	2	
Plumbing (GoGreen)		☐	Mon, Jul 29	5	
Electrical (KC Electric)		☐	Wed, Jul 31	5	
Framing		☐	Fri, Aug 2	1	
Floor Patching		☐	Fri, Aug 2	1	
Drywall		☐	Tue, Aug 6	5	
Shower Surround & Vanity Board Install		☐	Tue, Aug 6	2	
Fireplace Boarding		☐	Wed, Aug 7	1	
Taping & Sanding		☐	Wed, Aug 7	4	
Stairs & Railings		☐	Thu, Aug 8	5	
Stair Install		☐	Thu, Aug 8	5	
Flooring & Tiling		☐	Mon, Aug 12	19	
Tile Prep & Install		☐	Mon, Aug 12	15	
Hardwood Install		☐	Tue, Sep 3	4	
Cabinetry		☐	Fri, Aug 30	30	
Cabinet Delivery		☐	Fri, Aug 30	1	
Cabinet Install Pt.1 (Vanities)		☐	Tue, Sep 3	4	
Cabinet Install Pt.2 (Fireplace)		☐	Mon, Sep 9	1	
Cabinet Install Pt.2 (Kitchen)		☐	Fri, Oct 11	1	
Interior Finish		☐	Tue, Aug 6	58	
Deliver Trim Material (Regional)		☐	Tue, Aug 6	1	
Door Install (Regional/Blue Hammer)		☐	Mon, Aug 12	5	
Spray Trim and Doors		☐	Mon, Aug 19	5	
Trim Install (Regional/Blue Hammer)		☐	Mon, Sep 9	5	
Paint Prep (Rich Phillips)		☐	Mon, Sep 16	4	
Prep & Painting (Rich Phillips)		☐	Fri, Sep 20	8	
Garage Floor Finish (Garage Living)		☐	Mon, Sep 23	2	
Garage Wall/Cabinet Install (Garage Living)		☐	Thu, Sep 26	2	
Countertop Template		☐	Wed, Sep 11	1	
Shower Glass Template		☐	Tue, Sep 3	1	
Countertop Install		☐	Wed, Oct 2	2	
Shower Glass Install		☐	Fri, Oct 4	2	
Backsplash Install		☐	Mon, Oct 7	2	
Plumbing Finishes		☐	Wed, Oct 9	2	
Electrical Finishes		☐	Fri, Oct 11	2	
Staining (Rich Phillips)		☐	Wed, Oct 16	5	
Pre-Delivery Inspection		☐	Wed, Oct 23	1	
Clean-up & Final Touches		☐	Thu, Oct 24	3
